



Republic of the Philippines
Department of Education
REGION IV-A CALABARZON
SCHOOLS DIVISION OFFICE OF STO. TOMAS CITY

ACTIVITY PROPOSAL

**IN-HOUSE DEVELOPMENT OF AN INTEGRATED HUMAN RESOURCE
MANAGEMENT INFORMATION SYSTEM (IHRMIS)**

Targeting CSC PRIME-HRM Level 3 (Integrated)

Proponent Office:	SDO Sto. Tomas City – Office of the Schools Division Superintendent		
Program Name:	In-House Development of An Integrated Human Resource Management Information System (IHRMIS)		
Amount Requested:	Fifty-four thousand pesos (P 54,000.00)		
Rationale:	In the Schools Division Office (SDO) of Sto. Tomas City, human resource systems and processes are currently supported by a combination of standalone systems, spreadsheets, and manual procedures that operate in a fragmented manner, limiting data sharing and the generation of accurate, consolidated personnel information. The lack of a centralized and integrated HR system hampers the effective tracking and monitoring of key processes such as recruitment, performance management, learning and development, rewards and recognition, and personnel actions, resulting in inconsistent and inefficient operations across schools, offices, and units. Additionally, the continued reliance on paper-based and manual processes makes HR service delivery time-consuming, error-prone, and administratively burdensome, increasing the risk of data inaccuracies and non-compliance with DepEd policies, CSC guidelines, and PRIME-HRM requirements—thereby underscoring the need for an Integrated Human Resource Management Information System. At Level 3, HR systems are interconnected, data-driven, and consistently implemented. HR data is used for planning, monitoring, and improving organizational outcomes. As such, this proposal seeks approval for the in-house development of an Integrated Human Resource Management Information System (IHRMIS) designed to enable the Division to achieve and sustain CSC PRIME-HRM Level 3 (Integrated) status. The system will integrate HR core functions and support data-driven decision-making.		
II. A. Title of Activity: In-House Development of An Integrated Human Resource Management Information System (IHRMIS)			
A.1. Date of Conduct: June 22, 2026–March 22, 2026		A.2. Duration of the Activity: 9 months	
A.3. Venue/Platform: N/A		A.4. Target Participants: Development Team (1-3)	



Republic of the Philippines
Department of Education
REGION IV-A CALABARZON
SCHOOLS DIVISION OFFICE OF STO. TOMAS CITY

A.5. Activity Rationale:

The project shall address the need for the integration of all HR records and processes while maintaining compliance with DepEd, CSC, and Data Privacy policies.

A.6. Objectives:

The proposed Integrated Human Resource Management Information System aims to:

- Centralize and integrate HR data and systems to ensure accurate, timely, and consolidated personnel information across all schools and office units
- Improve the tracking and monitoring of key HR processes, including recruitment, performance management, learning and development, rewards and recognition, and personnel actions
- Streamline and automate HR workflows to reduce processing time, administrative burden, and reliance on paper-based systems
- Enhance data accuracy and minimize errors by reducing manual and redundant processes
- Strengthen compliance with DepEd policies, CSC guidelines, and PRIME-HRM Level 3 requirements through standardized and auditable processes
- Support data-driven decision-making through accessible reports, dashboards, and integrated HR analytics

A.7. Scope

The proposed Integrated Human Resource Management Information System (IHRMIS) will cover the key HR functions of the Schools Division Office of Sto. Tomas City. It will include modules for recruitment, performance management, learning and development, and rewards and recognition, ensuring that these processes are standardized and connected.

An Integrated Self-Service Portal will also be developed to allow employees, job applicants, teachers, school heads, and other personnel to directly access HR services. For job applicants, the portal will support functionalities such as online application submission, document upload, updating of applicant profiles, and tracking of application status. For employees and personnel, it will enable viewing and updating of personal records, submission of requests (e.g., leave and documents), tracking of transactions, and receipt of system notifications, thereby improving accessibility and transparency while reducing manual transactions.



Republic of the Philippines
Department of Education
REGION IV-A CALABARZON
SCHOOLS DIVISION OFFICE OF STO. TOMAS CITY

The system will also provide a centralized digital repository for employee records, replacing paper-based files and improving data accessibility. In addition, it will automate common HR workflows such as leave applications and personnel requests, making processes faster and more efficient.

An Integrated Payroll System may be included as an optional module, depending on organizational readiness and requirements. If implemented, its initial focus will be on ensuring the compatibility and migration of existing payroll data from the current system, allowing for future payroll integration while maintaining continuity and data integrity.

Finally, the IHRMIS will generate reports and basic analytics to support monitoring, decision-making, and compliance with CSC PRIME-HRM requirements across the Division and its schools.

A.8. Development Methodology

The development of the Integrated Human Resource Management Information System will adopt a **hybrid approach**, combining **Waterfall and Agile methodologies** to ensure structured planning, compliance with government standards, and flexibility in system development and improvement.

1. Overall System Approach (Waterfall Model)

The overall development of the IHRMIS will follow a **Waterfall model** to ensure a clear, sequential, and well-documented process aligned with DepEd and CSC requirements.

The major phases include:

- Requirements Analysis and Planning
- System Design and Architecture
- Development and Configuration
- Testing and Validation
- Deployment and Implementation
- Documentation and Compliance Support

2. Module Development Approach (Agile Model)

Individual system modules/subsystems (e.g., Recruitment, Performance Management, L&D, R&R) will be developed using an **Agile methodology** to allow iterative improvement and responsiveness to user needs.



Republic of the Philippines
Department of Education
REGION IV-A CALABARZON
SCHOOLS DIVISION OFFICE OF STO. TOMAS CITY

Each module will undergo:

- Sprint planning and prioritization
- Iterative development cycles
- Continuous testing and validation
- User feedback integration
- Incremental deployment

3. Task Management and Prioritization (Kanban Approach)

To support Agile implementation, the project will use the **3-Kanban system** for effective task management, visibility, and prioritization across the development lifecycle while maintaining compliance and alignment to organizational goals and policies.

The three Kanban boards, which represent stages of development, will be:

- **The Macro-Kanban (Portfolio Board)**

This Kanban board shall track initiatives and major projects instead of individual tasks, focusing on long term goals and sustainability. It shall have the columns **Exploration, Validation, Execution, and Harvest**. These columns serve as filters for projects, tracking them from proposals to deliberations to actual development and completion. For the purpose of this proposal, the PRIME-HRM-related projects shall take precedence over other projects.

- **The Team Kanban (Operational Board)**

This is the classic Kanban board that holds major tasks or deliverables from projects that get through to the Execution stage of the Macro-Kanban. It shall contain the following columns:

- **Backlog (To Do)**

Contains all identified system requirements, feature requests, and enhancement tasks. Items are prioritized based on urgency, PRIME-HRM relevance, and operational impact.

- **Development (In Progress)**

Tracks tasks currently being developed or configured. This board provides real-time visibility on workload, progress, and bottlenecks within the development team. A hard limit on the number of tasks shall be set on this column to prevent WIP (work-in-progress) overload, depending on the number of members on the development team and their capabilities.



Republic of the Philippines
Department of Education
REGION IV-A CALABARZON
SCHOOLS DIVISION OFFICE OF STO. TOMAS CITY

- **Completion (Done)**

Contains completed and tested features ready for deployment or already implemented. This serves as a record of deliverables and supports documentation for audit and reporting.

- **The Personal Kanban (Deep Work Board)**

The main purpose of this Kanban board is to manage cognitive load and prevent the **Zeigarnik Effect**, where uncompleted tasks are better remembered than completed ones. This board shall contain the specific tasks that need to be accomplished during the day or in a very short term. Its columns will be very similar to that of the Team Kanban with an additional column:

- **To Do**

Holds tasks assigned to an individual based on team tasks under development.

- **In Progress**

Contains tasks currently being executed.

- **Waiting**

Once a task is submitted for validation or forwarded to another team or member, it is moved to this column. Afterwards, it may be moved forward to Done or back to In Progress depending on feedback.

- **Done**

Column for completed tasks.

Key practices include:

- Limiting work-in-progress (WIP) to avoid overload
- Continuous reprioritization based on feedback and requirements
- Transparent tracking of tasks
- Alignment of tasks with module releases and PRIME-HRM deliverables

4. Integration and Data Synchronization

The methodology ensures strong system integration through:

- A unified employee database
- Standardized data structures and validation rules
- Cross-module data sharing and reporting

5. User Engagement and Change Management

- Regular consultations with HRMO and staff
- Pilot testing in selected units or schools



Republic of the Philippines
Department of Education
REGION IV-A CALABARZON
SCHOOLS DIVISION OFFICE OF STO. TOMAS CITY

- Training and capacity-building sessions
- Feedback and refinement cycles

6. Continuous Improvement

- Ongoing system evaluation and enhancement
- Updates based on policy changes and user needs
- Expansion of reporting and analytics features

A.9. Project Timeline

The development and implementation of the IHRMIS will be completed within an estimated **7 to 9 months**, following a **hybrid Waterfall-Agile approach supported by a 3-Kanban task management system**.

Phase	Description	Start	End	Duration
Phase 1	Requirements & Planning	Jun 22, 2026	Jul 21, 2026	1 month
Phase 2	System Design	Jul 22, 2026	Aug 21, 2026	1 month
Phase 3	Core System + Self-Service Portal	Aug 22, 2026	Oct 21, 2026	2 months
Phase 4	Core HR Modules (incl. MPaSIS 2.0)	Oct 22, 2026	Dec 21, 2026	2 months
Phase 5	Integration & Testing	Dec 22, 2026	Jan 21, 2027	1 month
Phase 6	Deployment & Training	Jan 22, 2027	Feb 21, 2027	1 month
Phase 7	Optional Enhancements (Payroll)	Feb 22, 2027	Mar 22, 2027	1 month
Total Duration				7-9 months

Phase 1: Requirements Analysis and Planning (Month 1)

(Waterfall Phase | Macro-Kanban: Exploration → Validation)

- Organization of project governance structure
- Identification of PRIME-HRM Level 3 requirements and gaps
- Documentation of HR workflows and user needs
- Registration/inclusion of the IHRMIS under the **Macro-Kanban (Exploration → Validation)**
- Initial population of the **Team Kanban Backlog (To Do)**

Output: Approved requirements and prioritized backlog

Phase 2: System Design and Architecture (Month 2)

(Waterfall Phase | Macro-Kanban: Validation → Execution)

- System architecture and database design
- UI/UX design
- Definition of core modules (Recruitment, Performance Management, L&D, R&R) and supporting components
- Integration planning and data standards



Republic of the Philippines
Department of Education
REGION IV-A CALABARZON
SCHOOLS DIVISION OFFICE OF STO. TOMAS CITY

- Backlog refinement in Team Kanban

Output: System design blueprint and development-ready plan

Phase 3: Core System and Self-Service Portal Development (Months 3–4)

(Waterfall + Agile | Team & Personal Kanban Active)

- Development of Core System and Employee Records Repository
- Development of the Integrated Self-Service Portal, including:
 - Employee access to records and requests
 - Applicant portal (application submission, document upload, status tracking)
 - Notifications and transaction monitoring
- Agile sprint cycles with continuous testing and feedback
- Task tracking via **Team Kanban (To Do → In Progress → Done)**
- Personal Kanban used for individual task execution

Output: Functional core system and operational self-service portal

Phase 4: Core HR Modules Development (Months 5–6)

(Agile + Kanban Execution)

- Development and integration of:
 - MPaSIS version 2.0 (Recruitment, Selection, and Placement Module)
 - Performance Management Module
 - Learning and Development (L&D) Module
 - Rewards and Recognition (R&R) Module
- Continuous Agile iterations, testing, and user feedback
- Cross-module integration with the core system and self-service portal
- Active use of Team and Personal Kanban for workflow control

Output: Fully developed and integrated HR modules

Phase 5: System Integration and Testing (Month 7)

(Waterfall + Agile Validation)

- Full system integration across all modules
- Functional, security, and data validation testing
- User Acceptance Testing (UAT) with HRMO and stakeholders
- Final validation through Team Kanban completion

Output: Integrated and validated IHRMIS (PRIME-HRM Level 3 ready)



Republic of the Philippines
Department of Education
REGION IV-A CALABARZON
SCHOOLS DIVISION OFFICE OF STO. TOMAS CITY

Phase 6: Deployment and Capacity Building (Month 8)

(Waterfall Phase | Macro-Kanban: Execution → Harvest)

- Pilot deployment within SDO units
- Training and orientation of users (HRMO, office and school personnel)
- Initial rollout and stabilization

Output: Operational IHRMIS with trained users


Phase 7: Optional Module Development and Enhancement (Month 9)

(Agile Continuity | Kanban-Driven)

- Development of **optional Integrated Payroll System**, if approved
 - Focus on **data compatibility and migration from existing payroll system**
- Enhancement of portal and reporting features
- Continuous improvements and user-driven refinements
- Finalization of PRIME-HRM documentation and evidence

Output: Enhanced system with optional payroll integration and optimized features

IHRMIS Project Gantt Chart (Top-Down Order)

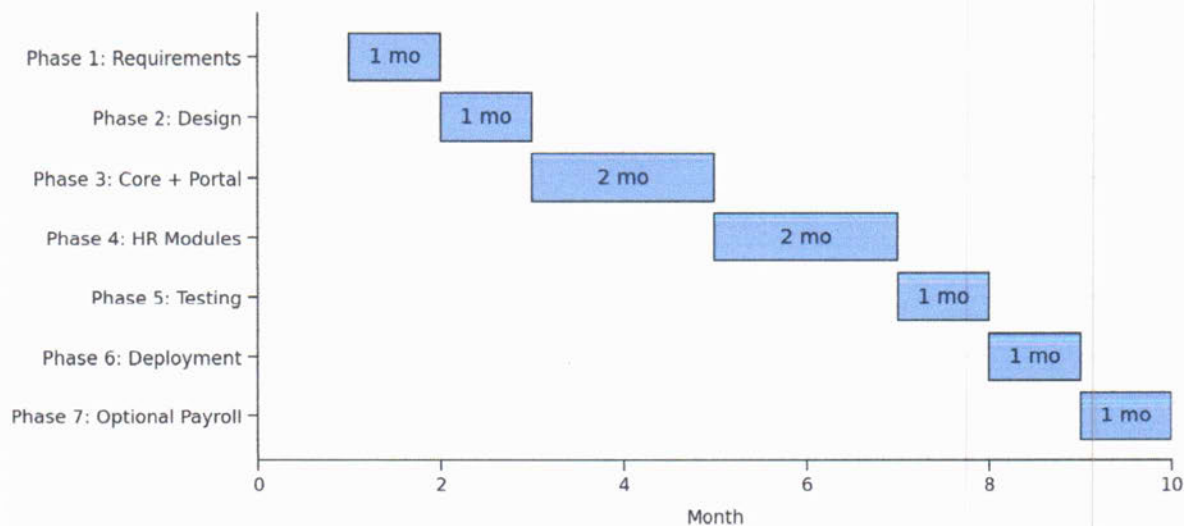



Republic of the Philippines
Department of Education
REGION IV-A CALABARZON
SCHOOLS DIVISION OFFICE OF STO. TOMAS CITY

A.10. Expected Outcomes

The successful development and implementation of the IHRMIS is expected to produce the following outcomes within SDO Sto. Tomas City:

- **Improved Efficiency and Service Delivery**
HR processes will become faster, more streamlined, and less dependent on manual and paper-based transactions, reducing administrative burden across all levels of the Division.
- **Centralized and Reliable HR Data**
A unified system will provide accurate, up-to-date, and consolidated personnel information, improving data integrity and accessibility for schools and SDO units.
- **Enhanced Monitoring and Process Standardization**
Key HR functions such as recruitment, performance management, learning and development, and personnel actions will be consistently implemented, tracked, and documented across the Division.
- **Strengthened Data-Driven Decision-Making**
Availability of reports, dashboards, and analytics will support evidence-based planning, workforce management, and compliance with CSC PRIME-HRM Level 3 requirements.
- **Established Governance Structure for HR Systems**
A clear governance framework will be institutionalized, defining roles and responsibilities among the SDO leadership, HRMO, PRIME-HRM Pillars, ICT unit, and end-users to ensure accountability, system sustainability, and continuous improvement.
- **Enhanced Data Privacy and Security Compliance**
The system will enforce data protection measures such as role-based access, secure storage, and audit trails, ensuring compliance with the Data Privacy Act of 2012 and safeguarding sensitive employee information.
- **Reduced Errors and Improved Compliance**
Automation and standardization will minimize manual errors and strengthen adherence to DepEd policies, CSC guidelines, and PRIME-HRM standards.
- **Readiness for PRIME-HRM Level 3 Certification**
The IHRMIS will support the documentation, integration, and utilization of HR systems required to achieve and sustain PRIME-HRM Level 3 (Integrated) maturity.



Republic of the Philippines
Department of Education
REGION IV-A CALABARZON
SCHOOLS DIVISION OFFICE OF STO. TOMAS CITY

A.11. Resource Requirements

The successful development and implementation of the Integrated Human Resource Management Information System (IHRMIS) will require a streamlined set of human, technical, organizational, and governance resources tailored to the operational context of SDO Sto. Tomas City.

1. Human Resources

Given the limited team size (1–3 personnel), system development roles will be combined to maximize efficiency while maintaining clear accountability:

- **Project Sponsor (Schools Division Superintendent) and Top Management**
Provide overall policy direction, strategic guidance, approvals, and institutional support, ensuring alignment of the project with organizational goals, priorities, and PRIME-HRM requirements
- **System Designer (Project Manager + System Analyst)**
Oversees project planning, requirements analysis, system design, and coordination with stakeholders
- **System Developer/Programmer**
Responsible for system development, database management, testing, and deployment
- **Information Technology Officer (ICT Officer)**
Provides infrastructure support, system administration, deployment assistance, and technical maintenance
- **Human Resource Management Officer (HRMO)**
Leads functional requirements validation and ensures alignment with HR policies and processes
- **PRIME-HRM Committees and Focal Persons**
Includes members and focal persons for:
 - Recruitment, Selection, and Placement (RSP)
 - Learning and Development (L&D)
 - Performance Management (PM)
 - Rewards and Recognition (R&R)



Republic of the Philippines
Department of Education
REGION IV-A CALABARZON
SCHOOLS DIVISION OFFICE OF STO. TOMAS CITY

These groups provide domain expertise, policy guidance, and ensure compliance with CSC PRIME-HRM standards

- **End Users**

Includes SDO personnel, school heads, teaching and non-teaching staff, and job applicants who will participate in testing, validation, and system use

2. Hardware Requirements

- Application and database server (on-site or cloud-based)
- Workstations or laptops for development and system access
- Reliable network infrastructure (internet connection, routers, switches)
- Backup storage devices for data redundancy

3. Software Requirements

- Development frameworks and programming tools
- Database Management System (DBMS) (e.g., MySQL, MariaDB)
- Web and application servers
- Version control tools (e.g., Git)
- Project management and Kanban tools
- Security tools (e.g., antivirus, encryption software)
- Office productivity software for documentation

4. Data and Information Resources

- Employee 201 records (digital and paper-based)
- HR datasets (recruitment, performance, L&D, R&R)
- Existing payroll data (for optional future integration)
- DepEd forms, templates, and reporting requirements
- CSC PRIME-HRM documentation and indicators

5. Policies, Standards, and Guidelines

- DepEd HR policies and operational procedures
- CSC PRIME-HRM framework and standards
- Civil Service Commission rules and regulations
- Data Privacy Act of 2012 (RA 10173)
- Government ICT and cybersecurity standards
- Internal SDO policies and workflows



Republic of the Philippines
Department of Education
 REGION IV-A CALABARZON
SCHOOLS DIVISION OFFICE OF STO. TOMAS CITY

6. Financial Resources

- Personnel support (if allowances or additional workload compensation is needed)
- Hardware and infrastructure setup or upgrades
- Software tools and licensing (if required)
- Training and capacity-building expenses
- Maintenance and system enhancement costs

7. Organizational and Operational Support

- Strong support from SDO leadership and management
- Active participation of HR units and PRIME-HRM committees
- Engagement of schools and functional units
- Training programs and user onboarding
- Monitoring and evaluation mechanisms for system performance

A.10. Budgetary Requirements

The estimated budget for the development and implementation of the Integrated Human Resource Management Information System (IHRMIS) is designed to reflect a **highly cost-efficient, in-house development approach**, maximizing the use of existing resources within SDO Sto. Tomas City.

1. Hardware and Infrastructure

Item	Description	Estimated Cost (PHP)
Desktop PC	Server for application and database hosting	49,000.00
Subtotal		49,000.00

2. Software and Tools

Item	Description	Estimated Cost (PHP)
SSL Certificate	Secure HTTPS access for the IHRMIS portal (mandatory for onsite hosting)	5,000.00
Subtotal		5,000.00

Total Estimated Budget

Items	Unit	Quantity	Unit Price	Total Amount
Desktop PC	unit	1	49,000.00	49,000.00
SSL Certificate	digital credential	1	5,000.00	5,000.00
TOTAL				P54,000.00



Republic of the Philippines
Department of Education
REGION IV-A CALABARZON
SCHOOLS DIVISION OFFICE OF STO. TOMAS CITY

Budget Notes and Justification

- The project adopts a fully in-house development strategy, utilizing existing personnel, infrastructure, and open-source or pre-existing software.
- No additional costs are allocated for personnel, software licensing, or infrastructure upgrades, ensuring a minimal and sustainable budget requirement.
- The SSL certificate is included as a mandatory requirement for onsite hosting to ensure secure system access and data protection.
- The desktop PC as a server is proposed to support scalability and performance while maintaining costs low but may be deferred or upgraded depending on needs and the capacity of existing infrastructure.
- The proposed budget may still be adjusted depending on feedback and other parameters, such as choosing between on-premises or cloud hosting, availing of a public IP address and/or a domain name, etc.

Prepared by:

GEOVANI P. DUQUEZA

Administrative Assistant III

Approved:

NEIL G. ANGELES, CESO V

Schools Division Superintendent
